
Construction Schedule of Main Access Tunnel (MAT)

Classic Schedule Layout

24-Sep-26 16:29

Activity ID	Activity Name	Original Duration	Start	Finish
UAHEP-MAT-CB-4	**Construction Schedule of Main Access Tunnel (MAT)**	715	08-Jun-26	11-Jun-28
UAHEP-MAT-CB-4.1	**Project Milestones**	535	14-Dec-26	11-Jun-28
A1000	Completion of the Bidding & Contractor Selection work	0		14-Dec-26
A1010	Signing of the Contract for Construction of MAT	0		15-Dec-26
A1020	Site Mobilization	0		19-Jan-27
A1030	Construction and Maintainance of Roads	0		03-Apr-27
A1040	Installation of Site Facilities	0		04-May-27
A1050	Completion of Major Pre-construction Activities	0		08-May-28
A1060	Construciton of the Main Access Tunnel (MAT)	0		07-May-28
A1070	Work Completion and Submission to the NEA	0		11-Jun-28
UAHEP-MAT-CB-4.2	**Pre-construction Activities**	0	08-May-28	08-May-28
UAHEP-MAT-CB-4.2.3	**Material Transport using Ferry**	0	08-May-28	08-May-28
A1100	Transporation of the heavy equipment for the MAT construction	0	08-May-28	08-May-28
UAHEP-MAT-CB-4.9	**Tendering Procedure & Contractor Selection**	180	08-Jun-26	14-Dec-26
A1300	Preparation and finalization of the bidding documents for MAT	70	08-Jun-26*	16-Aug-26
A1310	Finalization of the Bid evaluation/negotation reports for the Civil work of MAT	60	27-Aug-26	04-Nov-26
A1320	Contractor Selection	30	15-Nov-26	14-Dec-26
UAHEP-MAT-CB-4.8	**Contract Award**	1	15-Dec-26	15-Dec-26
A1400	Signing of Contract between the NEA and the Contractor of MAT (NBC)	1	15-Dec-26	15-Dec-26
UAHEP-MAT-CB-4.0	**Site Mobilization**	30	21-Dec-26	19-Jan-27
A1500	Mobilization of the Contractor after Signing of Contract	30	21-Dec-26	19-Jan-27
UAHEP-MAT-CB-4.3	**Site Installation**	60	06-Mar-27	04-May-27
A1600	Contractors Office	60	06-Mar-27	04-May-27
A1610	Contractors Camp/ Warehouse/Storage Yard	60	06-Mar-27	04-May-27
A1620	Facilities of aggregate production in the site	40	06-Mar-27	14-Apr-27
A1630	Construction of Field Laboratory	40	06-Mar-27	14-Apr-27
UAHEP-MAT-CB-4.4	**Construction Roads**	22	13-Mar-27	03-Apr-27
A1700	Temporary Haul Roads	22	13-Mar-27	03-Apr-27
UAHEP-MAT-CB-4.5	**Establishment of Muck Disposal Area**	0	13-Mar-27	13-Mar-27
A1800	Maintainance/Construction of the protection works in the Muck Disposal Area	0	13-Mar-27	13-Mar-27
UAHEP-MAT-CB-4.6	**Construction of Main Access Tunnel**	360	04-May-27	07-May-28
A1900	Portal development	90	04-May-27	01-Aug-27
A1910	Excavation in Heading	250	02-Aug-27	17-Apr-28
A1920	Excavation in Benching	130	20-Nov-27	28-Mar-28
A1930	Base preparation of invert level using muck/gravel material	40	29-Mar-28	07-May-28
A1940	Final finishing of MAT	30	08-Apr-28	07-May-28
UAHEP-MAT-CB-4.7	**Completion of Works**	35	08-May-28	11-Jun-28
A2000	Demobilization and Land refilling after site demolisation	34	08-May-28	10-Jun-28
A2010	Overall completion and submission of works to the NEA	1	11-Jun-28	11-Jun-28

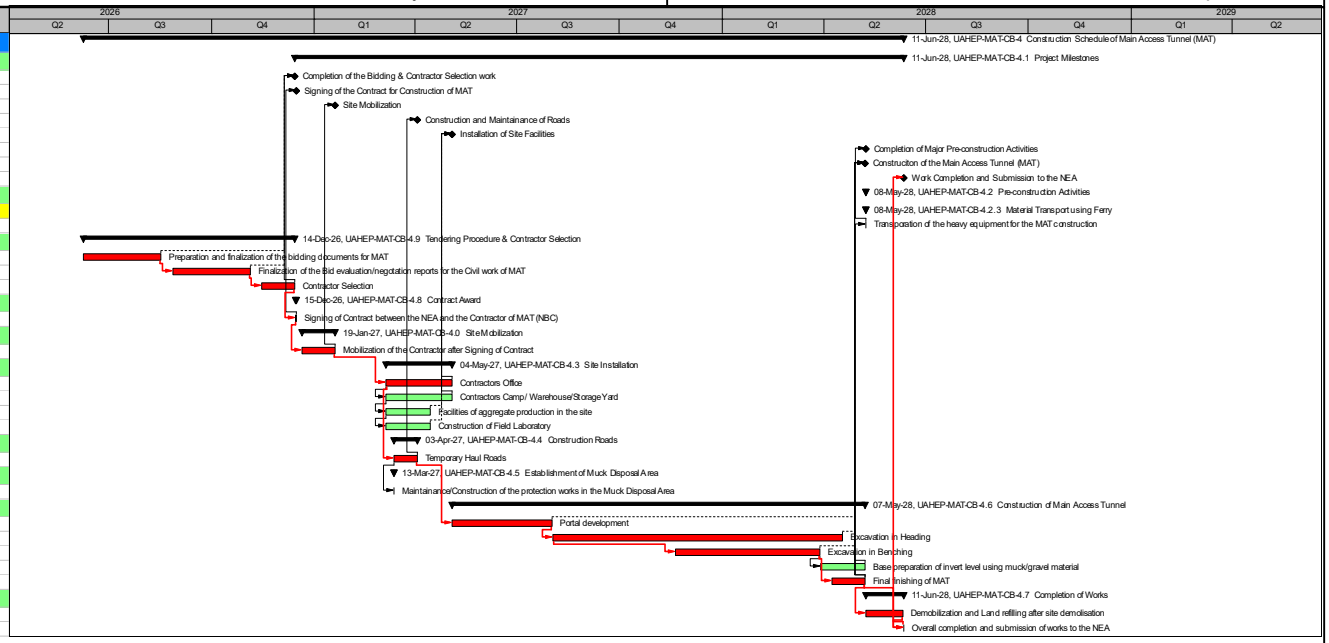

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaini...
Milestone
Summary

TASK filter: All Activities

© Oracle Corporation
