
Activity ID	Activity Name	Original Duration	Start	Finish
UAHEP-MAT-CB-2 Construction Schedule of Main Access Tur		806	08-Jun-26	15-Sep-28
UAHEP-MAT-CB-2.8 Project Milestones		626	14-Dec-26	15-Sep-28
A1164	Completion of Major Pre-construction Activities	0		22-Aug-27
A1165	Completion of the Bidding & Contractor Selection work	0		14-Dec-26
A1170	Signing of the Contract for Construction of MAT	0		15-Dec-26
A1180	Site Mobilization	0		19-Jan-27
A1190	Installation of Site Facilities	0		04-May-27
A1200	Construction and Maintainance of Roads	0		03-Apr-27
A1220	Construciton of the Main Access Tunnel (MAT)	0		06-Aug-28
A1230	Work Completion and Submission to the NEA	0		15-Sep-28
UAHEP-MAT-CB-2.10 Pre-construction Activities		510	06-Mar-27	07-Aug-28
UAHEP-MAT-CB-2.10.1 Construction of Access Road		170	06-Mar-27	22-Aug-27
A1270	Construction of the access road about 705 m (PH-R3, PH-R4 & PH-R7)	120	06-Mar-27*	03-Jul-27
A1340	Transportation of the material from storage area to the MAT inlet	50	04-Jul-27*	22-Aug-27
UAHEP-MAT-CB-2.10.3 Material Transport using Ferry		0	07-Aug-28	07-Aug-28
A1330	Transporation of the heavy equipment for the MAT construction	0	07-Aug-28	07-Aug-28
UAHEP-MAT-CB-2.9 Tendering Procedure & Contractor Select		180	08-Jun-26	14-Dec-26
A1240	Preparation and finalization of the bidding documents for MAT	70	08-Jun-26*	16-Aug-26
A1250	Finalization of the Bid evaluation/negotation reports for the Civil work of I	60	27-Aug-26	04-Nov-26
A1260	Contractor Selection	30	15-Nov-26	14-Dec-26
UAHEP-MAT-CB-2.1 Contract Award		1	15-Dec-26	15-Dec-26
A1000	Signing of Contract between the NEA and the Contractor of MAT (NBC)	1	15-Dec-26	15-Dec-26
UAHEP-MAT-CB-2.2 Site Mobilization		30	21-Dec-26	19-Jan-27
A1010	Mobilization of the Contractor after Signing of Contract	30	21-Dec-26	19-Jan-27
UAHEP-MAT-CB-2.3 Site Installation		60	06-Mar-27	04-May-27
A1020	Contractors Office	40	06-Mar-27	14-Apr-27
A1030	Contractors Camp/ Warehouse/Storage Yard	60	06-Mar-27	04-May-27
A1040	Facilities of aggregate production in the site	40	06-Mar-27	14-Apr-27
A1050	Construction of Field Laboratory	40	06-Mar-27	14-Apr-27
UAHEP-MAT-CB-2.4 Construction Roads		22	13-Mar-27	03-Apr-27
A1070	Temporary Haul Roads	22	13-Mar-27	03-Apr-27
UAHEP-MAT-CB-2.5 Establishment of Muck Disposal Area		0	13-Mar-27	13-Mar-27
A1080	Maintainance/Construction of the protection works in the Muck Disposal	0	13-Mar-27	13-Mar-27
UAHEP-MAT-CB-2.6 Construction of Main Access Tunnel		385	09-Jul-27	06-Aug-28
A1090	Portal development	60	09-Jul-27	06-Sep-27
A1100	Excavation in Heading	210	27-Sep-27	28-Apr-28
A1110	Excavation in Benching	100	29-Feb-28	07-Jun-28
A1130	Base preparation of invert level using muck/gravel material	40	08-Jun-28	17-Jul-28
A1140	Final finishing of MAT	30	08-Jul-28	06-Aug-28
UAHEP-MAT-CB-2.7 Completion of Works		35	07-Aug-28	15-Sep-28
A1155	Demobilization and Land refilling after site demolisation	34	07-Aug-28	09-Sep-28
A1160	Overall completion and submission of works to the NEA	1	15-Sep-28	15-Sep-28

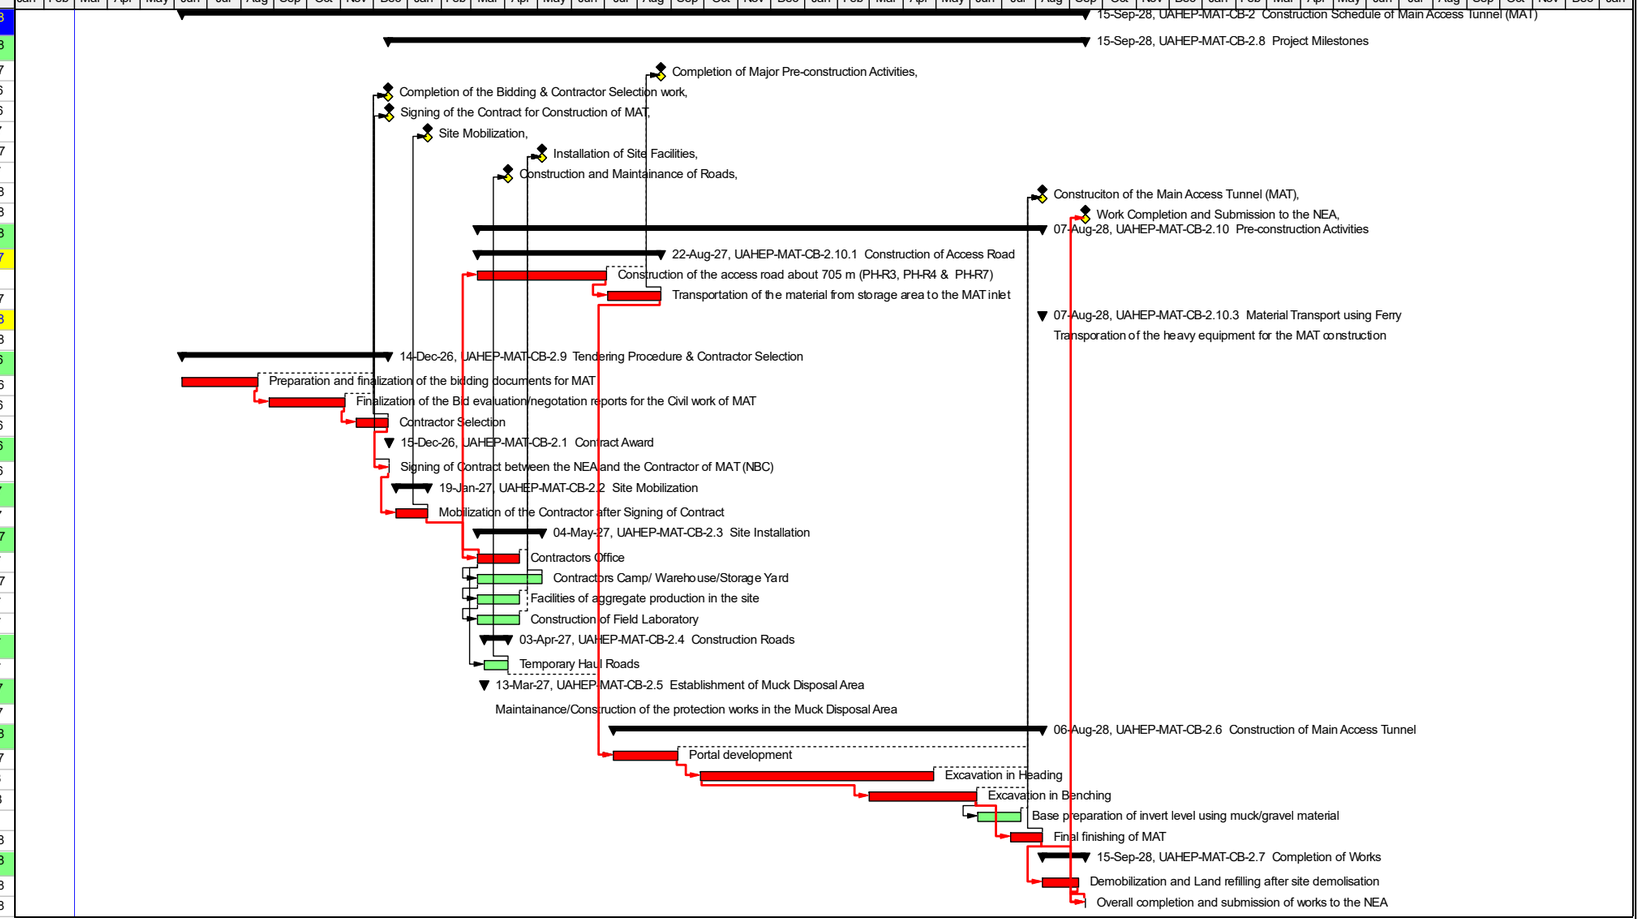

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Baseline Milestone | Milestone

TASK filter: All Activities

© Oracle Corporation
